
Lifting operations



TotalEnergies

6 fatalities related to lifting operations occurred within the Company in the last 10 years.

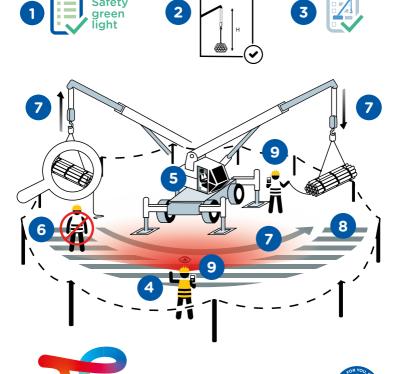

Lifting operations



Location	Date SAFETY Total English Park
Company observed	Permit No.
4ES 40 41A	POINTS TO BE CHECKED
	Has the "Safety green light" been carried out?
O O O 2	Is an approved lifting plan available?
3	Has the pre-start controls list been completed by the operations team at the beginning of the work?
004	Is the signaler/banksman appointed and recognizable?
5	Has the lifting appliance operator a training certificate / an authorization document to operate the appliance?
○ ○ 6	Is a restricted zone physically established and no one located under or in proximity of the suspended load?
O O 7	Is the lifting operation executed according to the lifting drawing / step-by-step procedure? (ex: slings, departure area, arrival area, overflown area)
8	Is no pressurized equipment present under or in proximity of the suspended load, except in specific cases addressed in the lifting plan?
O O 9	Is the moving load controled while being lifted?
Compliance rate (Nb	YES/applicable points): / (%)
Comments	
Name	Company
	Cianaturo
